


ID	Task Name	Duration	Start	Finish	Predecessors	2nd Half	1st Half	2nd Half	1st Half	2nd Half	1st Half	2nd Half	1st Half	2nd Half	1st Half	2nd Half	1st Half
1	Gloucester South West Bypass (Llanthony Road) Improvements																
2		1175 days?	Mon 03/04/17	Fri 01/10/21													
3	Full Business Case	232 days?	Mon 03/04/17	Tue 20/02/18													
4	Develop Options	40 days	Mon 03/04/17	Fri 26/05/17													
5	Agree Best Option	1 day	Mon 29/05/17	Mon 29/05/17	4												
6	Develop details for Public Share	26 days	Tue 30/05/17	Tue 04/07/17	5												
7	Public Share 1	1 day	Wed 05/07/17	Wed 05/07/17	6												
8	Public Share 2	1 day	Tue 11/07/17	Tue 11/07/17	7												
9	Submit FBC	8 days	Wed 12/07/17	Fri 21/07/17	8												
10	Receive comments and revise FBC	92 days	Mon 07/08/17	Tue 12/12/17	9												
11	Submit Final FBC	1 day	Wed 13/12/17	Wed 13/12/17	10												
12	FBC Approval by LEP	49 days	Thu 14/12/17	Tue 20/02/18	11												
13																	
14	Detailed Design Highways	808 days?	Tue 30/05/17	Thu 02/07/20													
15	Finalise Highway Alignment	113 days	Tue 30/05/17	Thu 02/11/17	5												
16	Fix min Land requirement	1 day	Fri 03/11/17	Fri 03/11/17	15												
17	Review TRO Requirement	15 days	Fri 08/12/17	Thu 28/12/17	15FS+25 days												
18	Progress any TROs (Assuming 12months)	255 days	Fri 12/07/19	Thu 02/07/20	17FS+400 days												
19	Highways Design	145 days	Mon 06/11/17	Fri 25/05/18	16												
20																	
21	Environmental Appraisals and Consents	99 days	Tue 24/10/17	Fri 09/03/18	19SS+30 days												
22																	
23	Land Purchase (Worse Case)	529 days	Tue 30/05/17	Fri 07/06/19	5												
24	Surveys & Building Design	179 days	Tue 30/05/17	Fri 02/02/18	5												
25	Planning Reg 3 Application	190 days	Mon 05/02/18	Fri 26/10/18	24												
26																	
27	Listed Building Consent (if required)	45 days	Mon 28/05/18	Fri 27/07/18													
28	Review if required	5 days	Mon 28/05/18	Fri 01/06/18	19												
29	Apply for consent	40 days	Mon 04/06/18	Fri 27/07/18	28												
30																	
31	Divert Statutory Services (gas/elec/water)	180 days	Mon 10/06/19	Fri 14/02/20	23												
32																	
33	Site Clearance	65 days	Mon 17/02/20	Fri 15/05/20	31												
34																	
35	Float	70 days	Mon 18/05/20	Fri 21/08/20	33												
36																	
37	Highways Site Works	290 days	Mon 24/08/20	Fri 01/10/21	35,18FF												
38																	

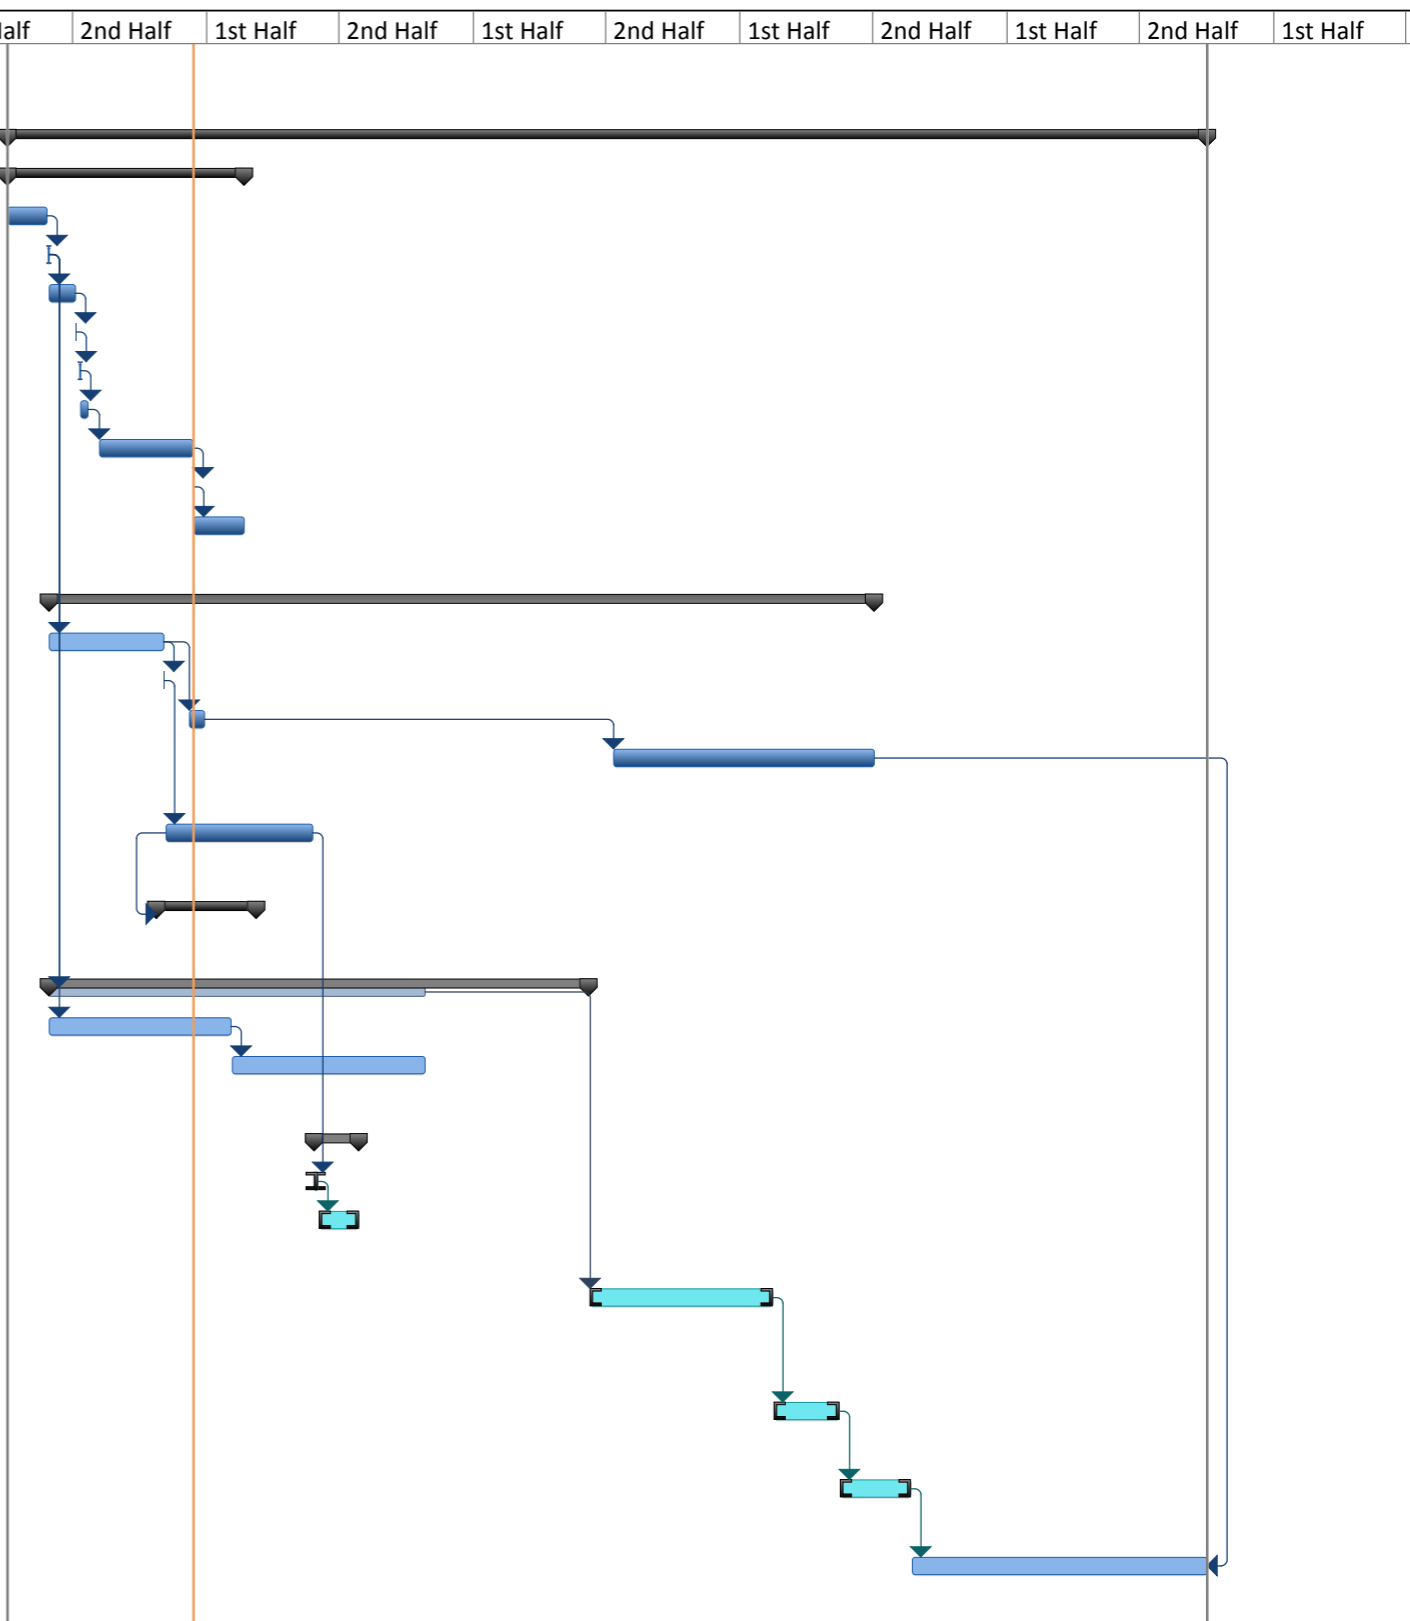

Project: GSWB Llanthony Overall P
Date: Thu 14/12/17

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			
