



# A435 Cheltenham Bishop's Cleeve Cycleway



Funded by  
UK Government

**Montel Civil Engineering** has been appointed by **Gloucestershire County Council** as the main contractor to complete Section 2 A435 Cheltenham to Bishop's Cleeve Cycleway.  
**Latest updates on the project as of 27th May 2025 are:**

## A435 Evesham Road/Wellington Road Junction

**The North East Cycleway** has been completed up to surface level and reopened, remaining works, including traffic signal installation and final surfacing, are planned for completion in early July.

### North East Corner


Traffic signal ducts and chambers have been completed.  
Street lighting column has now been relocated. New cycleway has been completed with raised levels to avoid damage to tree roots.

### North West Corner

Working area is being completed in two halves to maintain access to No.38 Park Hotel.  
We are now switching the access to the hotel, while we continue with site clearance and footway construction.

### South West Corner

Works have just commenced on traffic signal ducts and chambers.  
It is important to note that while we are continuing works in this corner the post box will be out of use whilst it is being relocated.

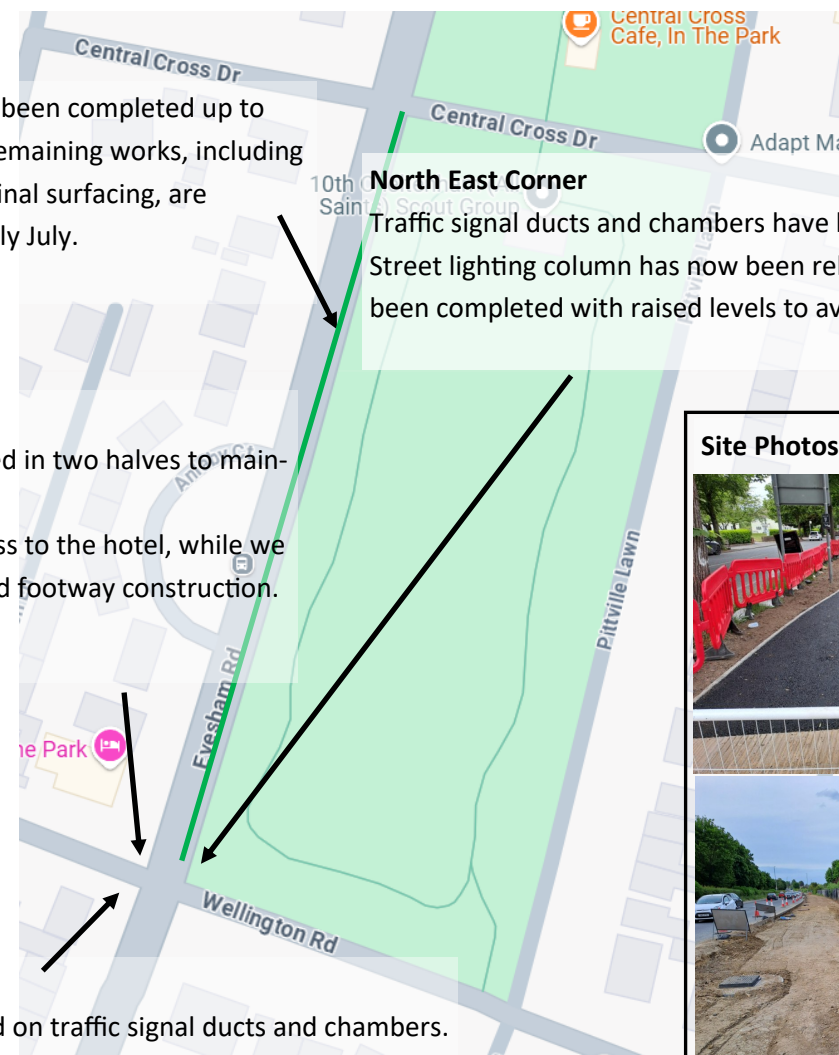

### Site Photos



Please contact [A435cycleway@montel-group.com](mailto:A435cycleway@montel-group.com) if you have any specific queries or concerns or would like to be added to the mailing list.





# A435 Cheltenham Bishop's Cleeve Cycleway



Funded by  
UK Government


## A435 Evesham Road (GWSR Bridge to Bishop's Cleeve roundabout)

**Northern Cycleway** Drainage activities have commenced on further section of the works. Electric cables have been adjusted and diverted to eliminate clashes with the drainage. **Severn Trent Water** have also completed main diversion. Formation of cycleway has now started.

**North East Corner** Minor Site clearance works have taken place. Main works have commenced on 12th May which include new traffic signal lights and cycleway construction.

**South East Corner** Drainage works are almost complete and cut and fill operations have started.

**Bishop's Cleeve Roundabout Works** due to commence early June.

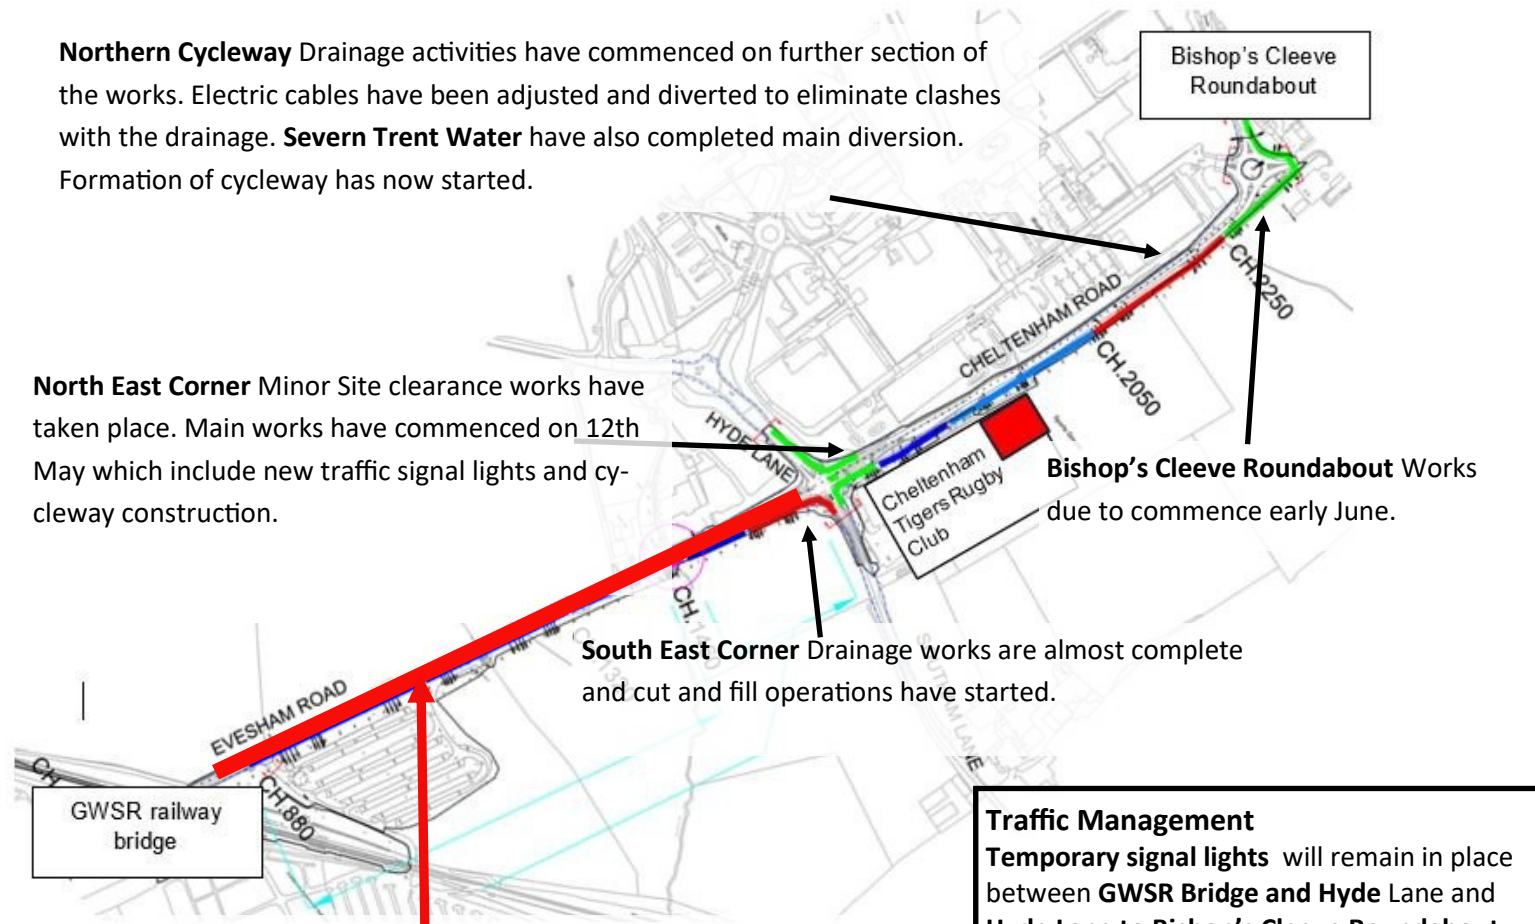

### Section 2.2(Cheltenham Racecourse Roundabout to GWSR Bridge)

Work commenced on 19th May with site preparation.

**A435 Road Closure:** On 2nd June a full road closure will be in place between Cheltenham Racecourse Roundabout and the Hyde Lane / Southam Lane junction. This will be in place until 8th September 2025, after which road will be reopened for Southbound traffic only and will remain closed for Northbound traffic until 31st October.

**Additionally** traffic signal engineers have been scheduled to be on-site on the first day of the closure to monitor traffic flow and to assess whether any adjustments are needed to the permanent signals on the A435 at the junction with Hyde Lane and Southam Lane.

### Traffic Management

**Temporary signal lights** will remain in place between **GWSR Bridge and Hyde Lane** and **Hyde Lane to Bishop's Cleeve Roundabout** until full Evesham Road closure on 2nd June.

**Wellington Road's temporary mini-roundabout** will remain in place through June and July.

**Stop/go boards** will continue to be in use during surfacing works.

*We will update you of any sudden changes on an ongoing basis, the next newsletter is due w/c 9th June.*

*We appreciate your continued patience and cooperation as we carry out these important improvements.*

Please contact [A435cycleway@montel-group.com](mailto:A435cycleway@montel-group.com) if you have any specific queries or concerns or would like to be added to the mailing list.

